Upper San Joaquin River Region Flood Management Plan Schedule

July 9, 2013
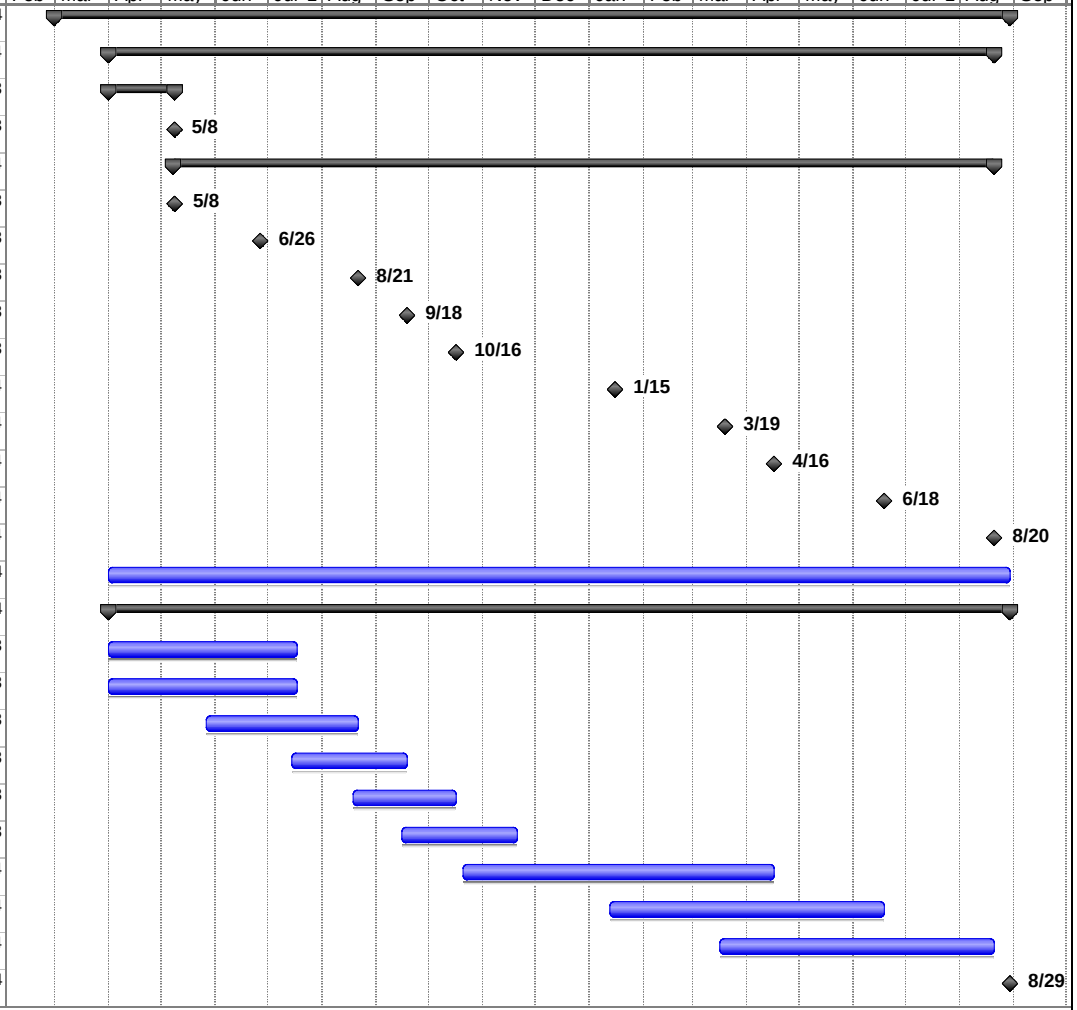
WBS	Task Name	Start	Finish
1	Project Administration and Work Plan	Fri 3/1/13	Fri 8/29/14
2	Coordination and Collaboration	Mon 4/1/13	Wed 8/20/14
2.1	Coordination and Collaboration	Mon 4/1/13	Wed 5/8/13
2.2	RFMP Planning Meetings	Wed 5/8/13	Wed 5/8/13
2.3	RFMP Workshops (10)	Wed 5/8/13	Wed 8/20/14
	Kick-Off Meeting	Wed 5/8/13	Wed 5/8/13
	Workshop 1 (Atlas, Flood Hazard, and Regional Setting)	Wed 6/26/13	Wed 6/26/13
	Workshop 2 (Land Use and Environment)	Wed 8/21/13	Wed 8/21/13
	Workshop 3 (ER Planning and Enhanced O&M)	Wed 9/18/13	Wed 9/18/13
	Workshop 4 (Proposed Improvements)	Wed 10/16/13	Wed 10/16/13
	Workshop 5 (Regional Priorities - Review Selection Criteria)	Wed 1/15/14	Wed 1/15/14
	Workshop 6 (Regional Priorities)	Wed 3/19/14	Wed 3/19/14
	Workshop 7 (Finance Plan)	Wed 4/16/14	Wed 4/16/14
	Workshop 8 (Draft RFMP)	Wed 6/18/14	Wed 6/18/14
	Workshop 9 (Final)	Wed 8/20/14	Wed 8/20/14
3	Update Regional Atlas	Mon 4/1/13	Fri 8/29/14
4	Develop Regional FMP	Mon 4/1/13	Fri 8/29/14
4.1	Regional Setting	Mon 4/1/13	Wed 7/17/13
4.2	Flood Hazards Assessment	Mon 4/1/13	Wed 7/17/13
4.3	Emergency Response Planning	Mon 5/27/13	Wed 8/21/13
4.4	Land Use and Environmental Enhancements	Mon 7/15/13	Wed 9/18/13
4.5	Enhanced Operations and Maintenance	Mon 8/19/13	Wed 10/16/13
4.6	Proposed Regional Improvements	Mon 9/16/13	Wed 11/20/13
4.7	Regional Priorities	Mon 10/21/13	Wed 4/16/14
4.8	Regional Financial Plan	Mon 1/13/14	Wed 6/18/14
4.9	Executive Summary and Plan Completion	Mon 3/17/14	Wed 8/20/14
4.10	Final Written Completion Report	Fri 8/29/14	Fri 8/29/14
